



**Free Questions for PK0-005 by [certsinside](#)**

**Shared by [Horton](#) on [29-01-2024](#)**

**For More Free Questions and Preparation Resources**

**[Check the Links on Last Page](#)**


# Question 1

---


**Question Type: MultipleChoice**

---

A project manager is monitoring team performance by comparing committed versus completed work. The project manager creates the following:

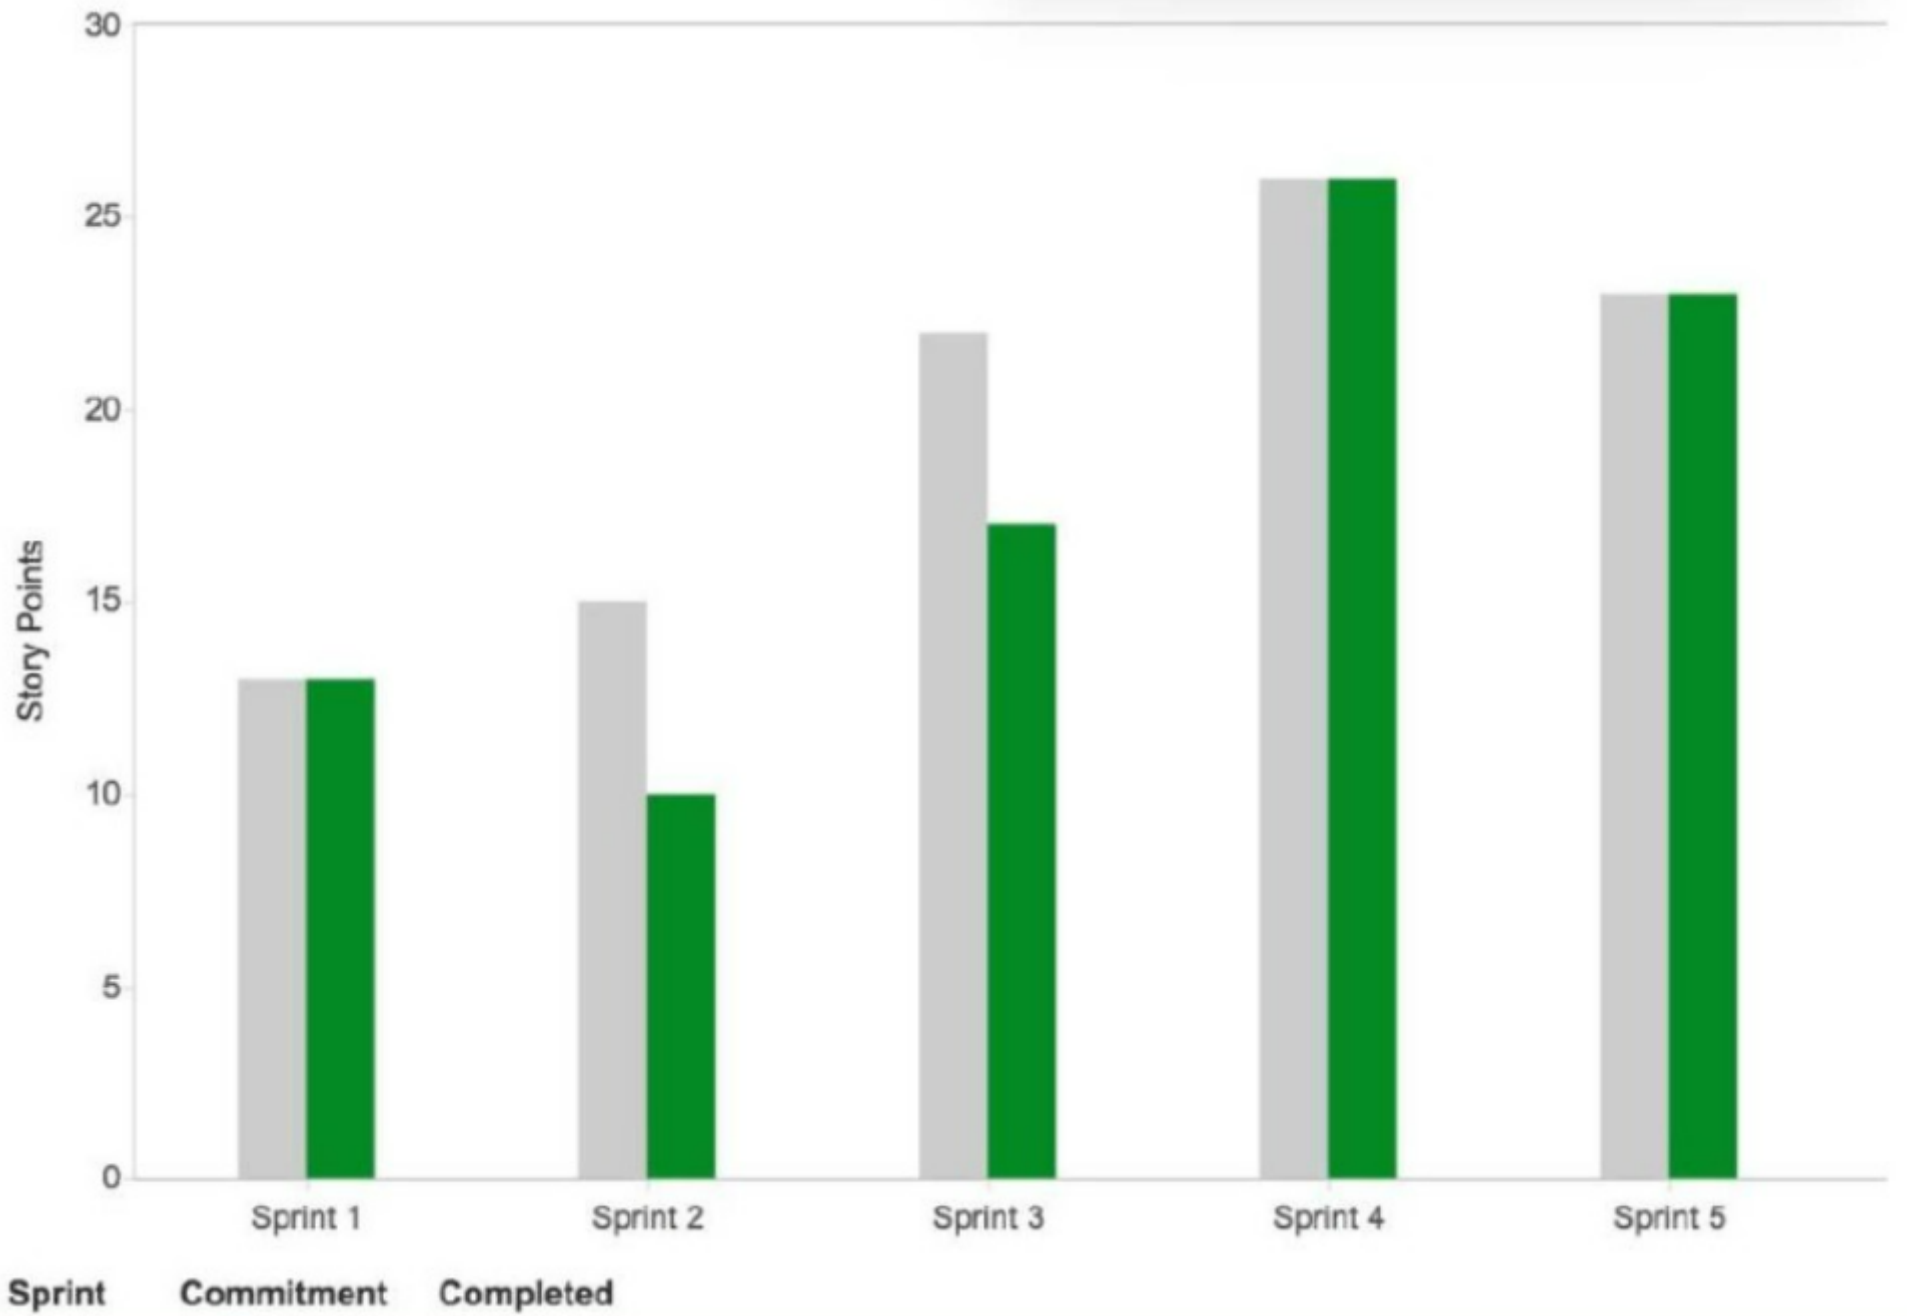

Sprint	Commitment	Completed
Sprint 1	13	13
Sprint 2	15	10
Sprint 3	22	17
Sprint 4	26	26
Sprint 5	23	23



Which of the following most likely represents the number of items in the backlog?

**Options:**

---

- A- 23
- B- 5
- C- 10
- D- 15

**Answer:**

---

A

### **Explanation:**

---

The number of items in the backlog can be determined by looking at the "Commitment" column for each sprint in the provided chart. For Sprint 5, there is a commitment of completing 23 items, which is the highest among all sprints. This indicates that there are at least 23 items in the backlog to be worked on. This is consistent with the concept of agile project management, which allows for changes and additions to the project scope based on customer feedback and changing requirements. Reference=CompTIA Project+ PK0-005 Certification Study Guide, Chapter 14: Agile Project Management, page 321. CompTIA Project+ Cert Guide: Exam PK0-004, Chapter 9: Agile Project Management, page 287

## **Question 2**

---

**Question Type: MultipleChoice**

---

After a migration was completed and a financial system was deployed, users have been unable to issue payment orders. Which of the following should be implemented?

**Options:**

---

- A- Rollback plan
- B- Release plan
- C- Deployment plan
- D- Contingency plan

**Answer:**

---

A

**Explanation:**

---

A rollback plan is a part of the project management plan that defines how to revert the system to its previous state or baseline if the change or migration fails or causes unacceptable impacts<sup>1</sup>. A rollback plan is different from a contingency plan, which is a plan to deal with a specific risk event that may or may not occur<sup>2</sup>. A release plan and a deployment plan are not relevant to the scenario, as they are used to plan and execute the delivery and installation of the system, not to undo them. Therefore, the correct answer is A. Rollback plan.

## Question 3

---

**Question Type:** MultipleChoice

---

Which of the following are primary features provided by a standard IaaS solution? (Select two).

### **Options:**

---

- A- Encryption
- B- Storage
- C- Networking
- D- User interface
- E- Access
- F- Database

### **Answer:**

---

B, C

### **Explanation:**

---

According to What is Logging as a Service (LaaS)? - LogicMonitor, LaaS is a cloud-based log management platform that simplifies the management of infrastructure and application logs. LaaS offers a central location where you can store, analyze and visualize the content of all your logs. It works by ingesting logs from different sources, such as web servers, IoT devices, database servers and more. It then provides actionable output by organizing and restructuring the information within these logs. Therefore, storage and networking are primary features provided by a standard LaaS solution, as they enable the collection and transmission of logs from various sources to a centralized platform. Encryption, user interface, access, and database are not primary features of LaaS, as they are either optional or secondary aspects of the service.

## Question 4

---

**Question Type:** MultipleChoice

---

Project stakeholders have asked the team to use Scrum to run a software implementation project. Which of the following is most likely to take place during a Scrum ceremony?

### Options:

---

- A- Reviewing project blockers
- B- Defining roles and responsibilities
- C- Establishing a project schedule
- D- Determining a project budget

### Answer:

---

A

### Explanation:

---



According to Four agile ceremonies, demystified, one of the Scrum ceremonies is the daily stand-up, which is a short meeting to discuss progress and identify blockers. Blockers are any issues or impediments that prevent the team from completing their tasks or achieving their goals. Reviewing project blockers during the daily stand-up helps the team to resolve them quickly, collaborate effectively, and stay on track<sup>1</sup>. The other options are not likely to take place during a Scrum ceremony, as they are either part of the initial project planning or outside the scope of Scrum.

## Question 5

---

**Question Type: MultipleChoice**

---

Following the approval of a change by the CCB, which of the following should a project manager consider next when deploying a new networking device into an existing production environment?

### Options:

---

- A- Maintenance window
- B- Risk assessment
- C- Operational security
- D- Validation check

**Answer:**

---

A

**Explanation:**

---

A maintenance window is a predefined period of time during which planned changes or updates can be performed on a system or network with minimal impact on the users or business operations<sup>1</sup>. A project manager should consider the maintenance window next when deploying a new networking device into an existing production environment, as it will help to reduce the risk of downtime, disruption, or errors. A maintenance window should be scheduled in advance, communicated to the stakeholders, and aligned with the change management plan<sup>2</sup>.

## Question 6

---

**Question Type: MultipleChoice**

---

A sponsor prefers to communicate with the team using email, phone calls, conversations in the hallway, and impromptu meetings. Which of the following types of communication is the sponsor using?

**Options:**

---

- A- Informal communication
- B- Formal communication
- C- Synchronous communication
- D- Asynchronous communication

**Answer:**

---

A

**Explanation:**

---

Informal communication is a type of communication that is casual, spontaneous, and unstructured. It does not follow any predefined rules, protocols, or formats. Examples of informal communication include email, phone calls, conversations in the hallway, and impromptu meetings<sup>12</sup>. The sponsor is using informal communication to communicate with the team, as these methods are convenient, flexible, and personal. However, informal communication may also have some drawbacks, such as lack of documentation, inconsistency, and potential for misunderstanding<sup>3</sup>. Therefore, the sponsor should also use formal communication when necessary, such as for official reports, contracts, and presentations<sup>4</sup>.

## Question 7

---

**Question Type: MultipleChoice**

---

Which of the following is a capital expense?

**Options:**

---

- A- Building lease
- B- Building purchase
- C- Building maintenance
- D- Building insurance

**Answer:**

---

B

**Explanation:**

---

A capital expense is the cost of acquiring or making improvements to fixed assets that have a useful life of more than one year<sup>1</sup>. A building purchase is an example of a capital expense, as it is a long-term investment that increases the value of the company's assets<sup>2</sup>. Building lease, maintenance, and insurance are not capital expenses, as they are recurring or short-term costs that do not increase the value of the company's assets<sup>3</sup>.

**To Get Premium Files for PK0-005 Visit**

**<https://www.p2pexams.com/products/pk0-005>**

**For More Free Questions Visit**

**<https://www.p2pexams.com/comptia/pdf/pk0-005>**

