



Download PeopleCert PRINCE2-Agile-Practitioner Exam Dumps Free

Shared by Bates on 17-06-2026

For More Free Questions and Preparation Resources

Check the Links on Last Page



Question 1

Question Type: MultipleChoice

Project scenario - Get fit with football!

(Note: The companies and people within the scenario are fictional)

Introduction

A Local Government Authority (LGA) has decided to organize a six-a-side football tournament. The tournament will contribute towards achieving the targets set by a national initiative to improve the fitness of children under the age of 16. As part of the LGA's policy of self-funding, this has to be achieved at zero cost to the LGA (and therefore the local tax payer). The cost of the event will be covered through fees paid by teams registered to take part in the tournament, sponsorship and monies raised during the day. Any surplus would be used for the maintenance of local sports centres.

Teams can register under one of several age groups for both boys and girls. In addition, family members are asked to attend to provide support.

This sports event is designed to be a family day out. The football tournament will have an event village including a kidz'-zone, catering, car parking, mobile changing rooms and toilets. The tournament will take place on the LGA-owned football pitches near the centre of the town, although space is somewhat limited.

Scope

The initial scope of the project includes:

The project has been set up with four work streams to deliver this work:


1. Marketing
2. Website
3. Event Village
4. Staff Training

Project Background

The LGA have extensive experience in using PRINCE2 and will run the event as a single project. The project manager is fully conversant with PRINCE2 Agile. One office in the LGA building in the centre of town has been given to the project for the entire duration. The office is across the corridor from the Marketing Department and the project manager has already put a sign on the door that says 'Mission Control'.

Timeline

An initial timeline has been suggested and is shown in the following diagram. The timeline may evolve due to the agile ways of working. The timeline shows how work streams are broken down into work packages and/or timeboxes.

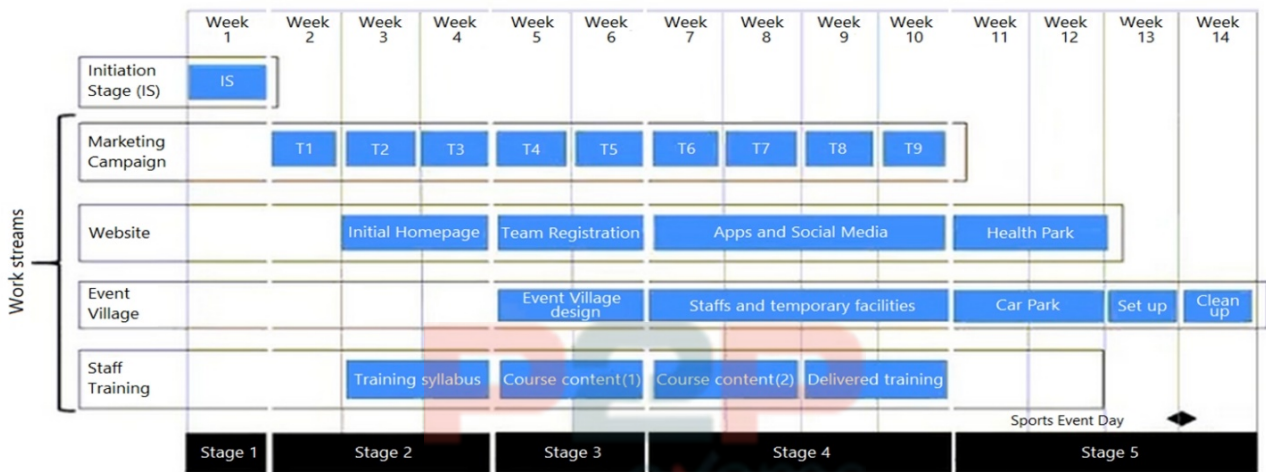

Website - Additional information

A new website will be built for the event. There are five work packages within this product:

1. Initial homepage:
2. Team Registration functionality:
3. Social media promoting the event and its aims.
4. Applications (apps) to promote healthy lifestyles including fitness and healthy eating apps.
5. Health Park:

The Website Team have a lot of experience in IT and have been using agile for several years. They are delivering the website through five two-week timeboxes. The team uses a Scrum Master to facilitate and the Scrum process and coach people accordingly.

The Website Team are very good at Scrum. They have created a set of tasks to assess more difficult work and they refer to this as sprint zero.

Using the Project Scenario and Website Additional information, answer the following question:

The Apps and Social Media work package includes the following requirements:

1. Fitness app - Must Have
2. Healthy eating app - Should Have

The burn-down chart is showing an ever-increasing negative gap between the ideal rate of progress and what has actually been delivered. The team manager decided not to deliver the healthy eating app. However, it is still forecast that requirement 1 cannot be completed within the current timebox.

The team manager escalated the issue to the project manager who instructed the team manager to immediately remove the burn-down chart from the information radiator.

What BEST explains how this approach applies the 'manage by exception' principle while taking into account the PRINCE2 Agile behaviours?

Options:

- A- It applies the principle well because the project manager will now decide how to proceed with the issue.
- B- It applies the principle well because the project manager's decision helps the Website Team self-organize within the constraints of the work package.
- C- It applies the principle poorly because the Website Team should be empowered to deal with issues relating to the work package.
- D- It applies the principle poorly because everyone in the Website Team should be aware that the work package is outside of tolerance.

Answer:

C

Explanation:

By removing the burn-down chart from the information radiator, the project manager limits the team's ability to visualize and manage their progress and challenges. In PRINCE2 Agile, teams should be empowered to handle issues within their work package, and transparency through tools like the burn-down chart is essential for self-management and collaboration.

Question 2

Question Type: MultipleChoice

Project scenario - Get fit with football!

(Note: The companies and people within the scenario are fictional)

Introduction

A Local Government Authority (LGA) has decided to organize a six-a-side football tournament. The tournament will contribute towards achieving the targets set by a national initiative to improve the fitness of children under the age of 16. As part of the LGA's policy of self-funding, this has to be achieved at zero cost to the LGA (and therefore the local tax payer). The cost of the

event will be covered through fees paid by teams registered to take part in the tournament, sponsorship and monies raised during the day. Any surplus would be used for the maintenance of local sports centres.

Teams can register under one of several age groups for both boys and girls. In addition, family members are asked to attend to provide support.

This sports event is designed to be a family day out. The football tournament will have an event village including a kidz'-zone, catering, car parking, mobile changing rooms and toilets. The tournament will take place on the LGA-owned football pitches near the centre of the town, although space is somewhat limited.

Scope

The initial scope of the project includes:

The project has been set up with four work streams to deliver this work:


1. Marketing
2. Website
3. Event Village
4. Staff Training

Project Background

The LGA have extensive experience in using PRINCE2 and will run the event as a single project. The project manager is fully conversant with PRINCE2 Agile. One office in the LGA building in the centre of town has been given to the project for the entire duration. The office is across the corridor from the Marketing Department and the project manager has already put a sign on the door that says 'Mission Control'.

Timeline

An initial timeline has been suggested and is shown in the following diagram. The timeline may evolve due to the agile ways of working. The timeline shows how work streams are broken down into work packages and/or timeboxes.

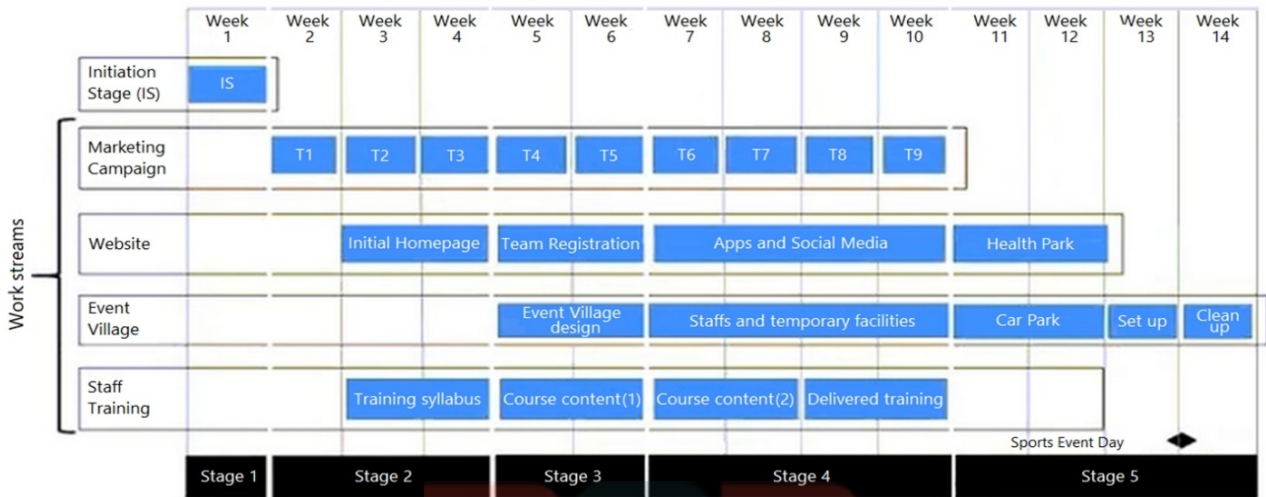

Marketing - Additional information

The marketing campaign has two key areas to promote:

1. The event itself including the football tournament, event village and fundraising activities.
2. The LGA's long term aim to improve the fitness of children under the age of 16.

The Marketing Team has received some initial Scrum training but is unsure how it can be applied to their marketing work.

The Marketing Team is keen that the project manager provides them with a clear brief for the campaign before they spend too much time on it.

They have experience of working with a variety of marketing channels, although they are not sure which channel(s) will work most effectively to promote this type of event, and in particular to promote the LGA's longer term health aims.

The Marketing Team is not clear on the priority to assign to the two aims for the event.

The Marketing Team will publish advertisements and/or promotional material every week, with more information in each issue to keep the message up to date.

Nine releases are scheduled at the end of each of the nine week-long timeboxes.

The nine timeboxes within the marketing work stream are scheduled to include:

Using the Project Scenario and Marketing Additional information, answer the following question:

The project manager recommends that Stage 2 should be broken down further with more stage boundaries linked to the weekly publication of a newspaper advertisement.

Using the Timeline, which statement BEST evaluates this proposal in relation to the 'manage by stages' principle?

Options:

- A- It applies the principle well because short stage boundaries provide more opportunity for inter-team collaboration.
- B- It applies the principle well because short stage boundaries will enable the project to fail-fast and learn-fast.
- C- It applies the principle poorly because stage boundaries should be set at the beginning of each new timebox.
- D- It applies the principle poorly because the stage boundaries should typically be monthly on a three-month project.

Answer:

B

Explanation:

The 'manage by stages' principle emphasizes breaking the project into manageable stages to assess progress and adapt as necessary. By creating shorter stage boundaries linked to the weekly publication of advertisements, the project can quickly identify issues and adjust strategies, fostering a learn-fast approach.

Question 3

Question Type: MultipleChoice

What does PRINCE2 Agile identify as a 'concept'?

Options:

- A- Prioritizing what needs to be delivered.
- B- Trusting and not blaming others.
- C- Setting tolerances for each project objective to establish limits of authority.
- D- Using daily stand-up meetings and user stories.

Answer:

D

Explanation:

This option reflects key practices in Agile methodologies, emphasizing collaboration and iterative progress, which are central to Agile principles.

Question 4

Question Type: MultipleChoice

Project scenario - Get fit with football!

(Note: The companies and people within the scenario are fictional)

Introduction

A Local Government Authority (LGA) has decided to organize a six-a-side football tournament. The tournament will contribute towards achieving the targets set by a national initiative to improve the fitness of children under the age of 16. As part of the LGA's policy of self-funding, this has to be achieved at zero cost to the LGA (and therefore the local tax payer). The cost of the event will be covered through fees paid by teams registered to take part in the tournament, sponsorship and monies raised during the day. Any surplus would be used for the maintenance of local sports centres.

Teams can register under one of several age groups for both boys and girls. In addition, family members are asked to attend to provide support.

This sports event is designed to be a family day out. The football tournament will have an event village including a kidz'-zone, catering, car parking, mobile changing rooms and toilets. The tournament will take place on the LGA-owned football pitches near the centre of the town, although space is somewhat limited.

Scope

The initial scope of the project includes:

The project has been set up with four work streams to deliver this work:


1. Marketing
2. Website
3. Event Village
4. Staff Training

Project Background

The LGA have extensive experience in using PRINCE2 and will run the event as a single project. The project manager is fully conversant with PRINCE2 Agile. One office in the LGA building in the centre of town has been given to the project for the entire duration. The office is across the corridor from the Marketing Department and the project manager has already put a sign on the door that says 'Mission Control'.

Timeline

An initial timeline has been suggested and is shown in the following diagram. The timeline may evolve due to the agile ways of working. The timeline shows how work streams are broken down into work packages and/or timeboxes.

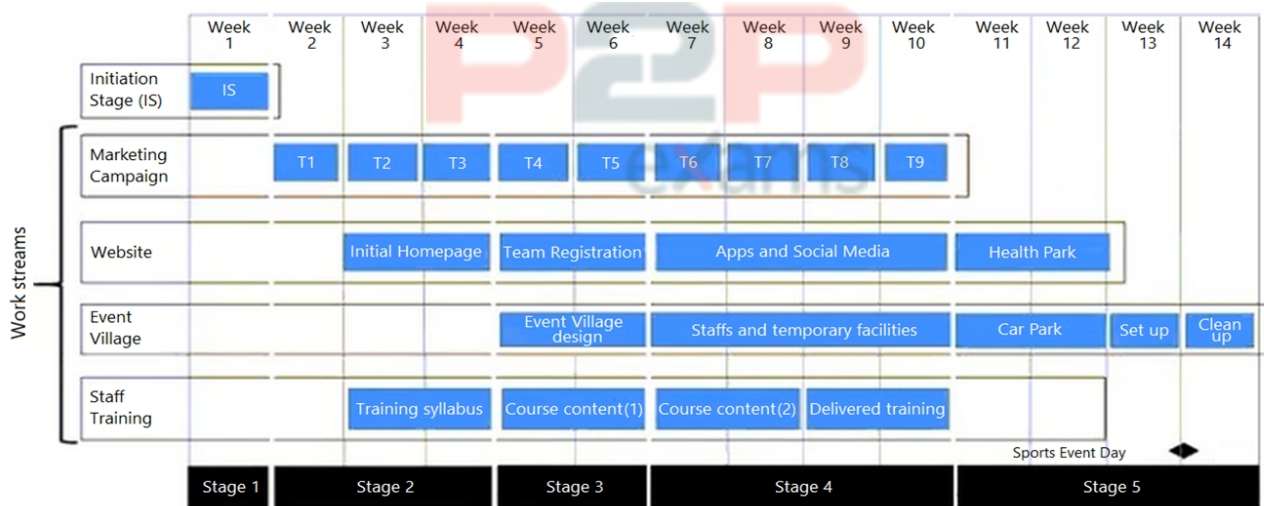

Marketing - Additional information

The marketing campaign has two key areas to promote:

1. The event itself including the football tournament, event village and fundraising activities.
2. The LGA's long term aim to improve the fitness of children under the age of 16.

The Marketing Team has received some initial Scrum training but is unsure how it can be applied to their marketing work.

The Marketing Team is keen that the project manager provides them with a clear brief for the campaign before they spend too much time on it.

They have experience of working with a variety of marketing channels, although they are not sure which channel(s) will work most effectively to promote this type of event, and in particular to promote the LGA's long term health aims.

The Marketing Team is not clear on the priority to assign to the two aims for the event.

The Marketing Team will publish advertisements and/or promotional material every week, with more information in each issue to keep the message up to date.

Nine releases are scheduled at the end of each of the nine week-long timeboxes.

The nine timeboxes within the marketing work stream are scheduled to include:

Using the Project Scenario and Marketing Additional information, answer the following question:

Nine timeboxes are scheduled for the marketing work.

Which baseline product is MOST relevant for defining which marketing product will be released in each timebox?

Options:

- A- Business case.
- B- Project product description.
- C- Project brief.
- D- Work package.

P2P
exams

Answer:

B

Explanation:

The project product description outlines the key deliverables of the project and their acceptance criteria. This product serves as a reference for the marketing team to determine which marketing products should be delivered in each timebox, ensuring that all releases align with the overall project goals.

Question 5

Question Type: MultipleChoice

P2P
exams

Project scenario - Get fit with football!

(Note: The companies and people within the scenario are fictional)

Introduction

A Local Government Authority (LGA) has decided to organize a six-a-side football tournament. The tournament will contribute towards achieving the targets set by a national initiative to improve the fitness of children under the age of 16. As part of the LGA's policy of self-funding, this has to be achieved at zero cost to the LGA (and therefore the local tax payer). The cost of the event will be covered through fees paid by teams registered to take part in the tournament, sponsorship and monies raised during the day. Any surplus would be used for the maintenance of

local sports centres.

Teams can register under one of several age groups for both boys and girls. In addition, family members are asked to attend to provide support.

This sports event is designed to be a family day out. The football tournament will have an event village including a kidz'-zone, catering, car parking, mobile changing rooms and toilets. The tournament will take place on the LGA-owned football pitches near the centre of the town, although space is somewhat limited.

Scope

The initial scope of the project includes:

The project has been set up with four work streams to deliver this work:


1. Marketing
2. Website
3. Event Village
4. Staff Training

Project Background

The LGA have extensive experience in using PRINCE2 and will run the event as a single project. The project manager is fully conversant with PRINCE2 Agile. One office in the LGA building in the centre of town has been given to the project for the entire duration. The office is across the corridor from the Marketing Department and the project manager has already put a sign on the door that says 'Mission Control'.

Timeline

An initial timeline has been suggested and is shown in the following diagram. The timeline may evolve due to the agile ways of working. The timeline shows how work streams are broken down into work packages and/or timeboxes.

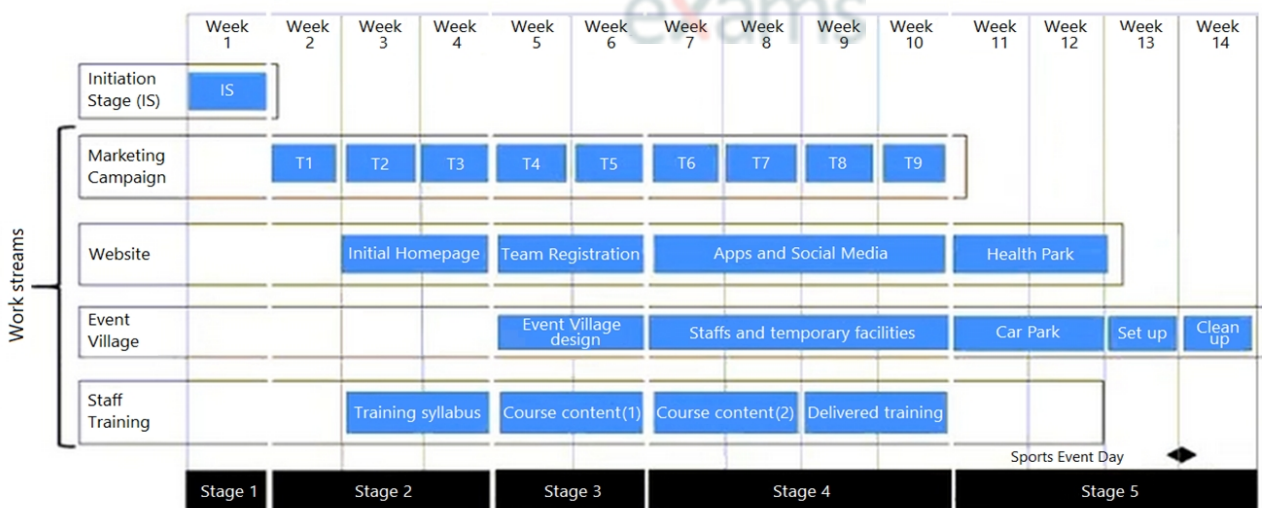

Marketing - Additional information

The marketing campaign has two key areas to promote:

1. The event itself including the football tournament, event village and fundraising activities.
2. The LGA's long term aim to improve the fitness of children under the age of 16.

The Marketing Team has received some initial Scrum training but is unsure how it can be applied to their marketing work.

The Marketing Team is keen that the project manager provides them with a clear brief for the campaign before they spend too much time on it.

They have experience of working with a variety of marketing channels, although they are not sure which channel(s) will work most effectively to promote this type of event, and in particular to promote the LGA's longer term health aims.

The Marketing Team is not clear on the priority to assign to the two aims for the event.

The Marketing Team will publish advertisements and/or promotional material every week, with more information in each issue to keep the message up to date.

Nine releases are scheduled at the end of each of the nine week-long timeboxes.

The nine timeboxes within the marketing work stream are scheduled to include:

Using the Project Scenario and Marketing Additional information, answer the following question:

Many Marketing Team members were expressing frustration that some members of the team had worked only on specific products and had not helped in the delivery of others. Therefore, the Marketing Team produced a Glad! Sad! Mad! board during a recent retrospective.

Which statement explains why this approach to identifying issues is appropriate for the 'controlling a stage' process?

Options:

- A- A retrospective should identify all areas of improvement that should be actioned by a team.
- B- Glad! Sad! Mad! is a feedback technique that focuses on feelings and helps to identify improvements.
- C- Glad! Sad! Mad! is a feedback technique used in a retrospective to monitor the progress of a team.
- D- The retrospective empowers the delivery teams to work with a visual approach during a timebox.

Answer:

B

Explanation:

The Glad! Sad! Mad! board allows team members to express their feelings about their experiences during the stage, helping to surface issues and areas for improvement. This emotional feedback can be crucial in identifying specific challenges within the team dynamics and product delivery, facilitating better control and adjustments for future stages.

Question 6

Question Type: MultipleChoice

Which BEST describes an agile method or approach that can be integrated with PRINCE2 Agile?

Options:

- A- Encouraging system improvement through visualization and controlling work in progress.
- B- Providing guidance on tailoring any applicable principles, themes and processes.
- C- Reducing quality testing in order to deliver within agreed deadlines.
- D- Favoring processes and tools over individuals and interactions.

Answer:

A

Explanation:

This approach aligns with Agile principles, emphasizing continuous improvement and effective workflow management, which can complement the structured framework of PRINCE2 Agile.

Question 7

Question Type: MultipleChoice

Which is a benefit that can be realized by a PRINCE2 organization seeking to adopt PRINCE2 Agile?

Options:

- A- Comprehensive documentation is reduced as working software is a priority.
- B- Reduced number of roles by combining project manager with team manager.
- C- Lower cost of ownership throughout the life of the project's delivered product(s).
- D- Improved maintenance of a business case throughout the project

Answer:

A

Explanation:

This benefit reflects the Agile principle of prioritizing working software over extensive documentation, which can lead to more efficient project delivery.

Question 8

Question Type: MultipleChoice

Project scenario - Get fit with football!

(Note: The companies and people within the scenario are fictional)

Introduction

A Local Government Authority (LGA) has decided to organize a six-a-side football tournament. The tournament will contribute towards achieving the targets set by a national initiative to improve the fitness of children under the age of 16. As part of the LGA's policy of self-funding, this has to be achieved at zero cost to the LGA (and therefore the local tax payer). The cost of the event will be covered through fees paid by teams registered to take part in the tournament, sponsorship and monies raised during the day. Any surplus would be used for the maintenance of local sports centres.

Teams can register under one of several age groups for both boys and girls. In addition, family members are asked to attend to provide support.

This sports event is designed to be a family day out. The football tournament will have an event village including a kidz'-zone, catering, car parking, mobile changing rooms and toilets. The tournament will take place on the LGA-owned football pitches near the centre of the town, although space is somewhat limited.

Scope

The initial scope of the project includes:

The project has been set up with four work streams to deliver this work:


1. Marketing
2. Website
3. Event Village
4. Staff Training

Project Background

The LGA have extensive experience in using PRINCE2 and will run the event as a single project. The project manager is fully conversant with PRINCE2 Agile. One office in the LGA building in the centre of town has been given to the project for the entire duration. The office is across the corridor from the Marketing Department and the project manager has already put a sign on the door that says 'Mission Control'.

Timeline

An initial timeline has been suggested and is shown in the following diagram. The timeline may evolve due to the agile ways of working. The timeline shows how work streams are broken down into work packages and/or timeboxes.

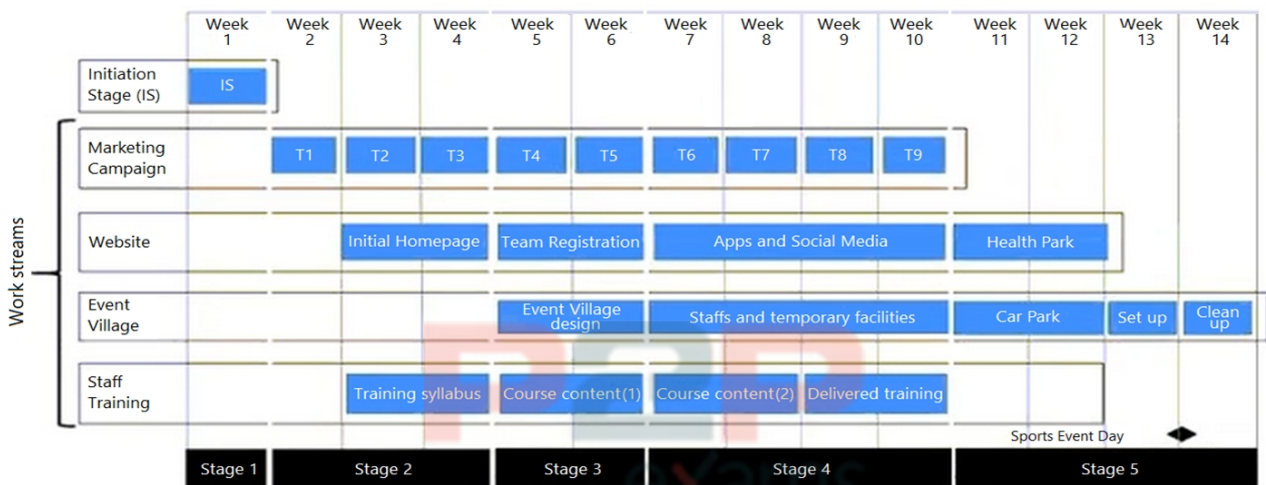

Website - Additional information

A new website will be built for the event. There are five work packages within this product:

1. Initial homepage:
2. Team Registration functionality:
3. Social media promoting the event and its aims.
4. Applications (apps) to promote healthy lifestyles including fitness and healthy eating apps.

5. Health Park:

The Website Team have a lot of experience in IT and have been using agile for several years. They are delivering the website through five two-week timeboxes. The team uses a Scrum Master to facilitate and the Scrum process and coach people accordingly.

The Website Team are very good at Scrum. They have created a set of tasks to assess more difficult work and they refer to this as sprint zero.

Using the Project Scenario and Website Additional information, answer the following question:

The project manager has asked the Scrum Master who will be leading the website work stream to act as team manager. The team manager will act as a single point of contact for the project manager, taking on the responsibilities of a team manager. The team manager will continue to coach and lead the Website Team.

Which BEST describes how this tailors the organization theme?

Options:

- A- The Scrum Master should serve the Scrum team while taking on the responsibilities of a team manager.
- B- The project manager wants the Website Team to use fewer agile behaviours than they are currently using.
- C- Each person in the Website Team, including the Scrum Master, should be capable of performing multiple tasks.
- D- There should only be one team in a small scale project with the Website Team taking on all of the delivery roles.

Answer:

A

Explanation:

By having the Scrum Master act as the team manager, it emphasizes the role of the Scrum Master in supporting and serving the team while also managing the communication and responsibilities required by the project manager. This approach maintains agile principles while ensuring clarity in roles and responsibilities within the team.

To Get Premium Files for PRINCE2-Agile-Practitioner Visit

<https://www.p2pexams.com/products/prince2-agile-practitioner>



For More Free Questions Visit

<https://www.p2pexams.com/peoplecert/pdf/prince2-agile-practitioner>

20%
DISCOUNT

